




Colony Park Drainage Project

Date Last Edited: Wednesday, May 13, 2015

Colony Park Drainage Park – City of Gulfport In-House Project



Placing precast inlet at Gulf Ave 2-10-15.

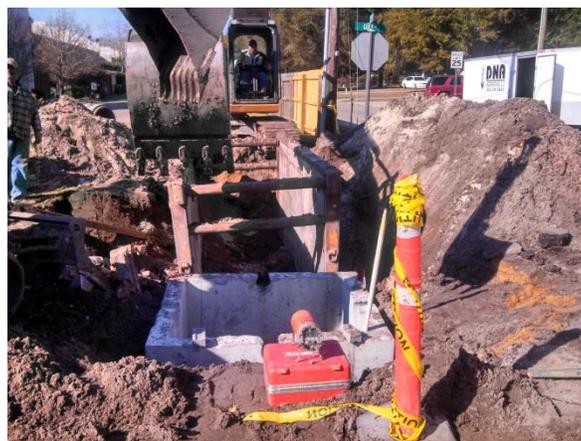

Crew Preparing to lay more 36" pipe. Six hundred forty feet are now in the ground.

1-14-15: First joint of 42" pipe placed. The project is on the way



Date 1-13-15. Crew breaks into starting inlet to begin laying 42" concrete pipe





Date 1-22-15. Crew sets junction box\inlet to clear live oaks on the project. Pipe size is 42" concrete.



Date: 1-30-15. Crew is near the end of laying 42" concrete pipe. Backfill operation is taking place.



2-2-15. Crew sets inlet box. Completes laying 42" concrete pipe and begins laying 36" pipe
